



Rosedale Highway facing east— December 2015

Kern Council of Governments

Progress Report for Projects of Regional Significance

OCTOBER 2016 EDITION

**This report is updated quarterly
and posted on the Kern COG
website at www.kerncog.org**



What's Inside?

Status Information on:

Constructed Projects

Safety & Maintenance

New Construction

Metro. Bakersfield Projects

Projects throughout County



Questions or comments?

Please contact:

Joe Stramaglia
jstramaglia@kerncog.org
661-635-2914



THANK YOU...


*to our Caltrans and local
project managers and
planning staff who
contribute to this report.*



PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Countywide - Highway Safety and Maintenance

I-5 - PM 54.1 - Buttonwillow - Safety Roadside Rest Area - Upgrade Water and Waste Water Systems

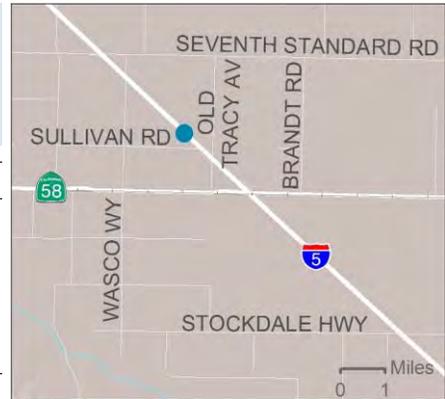


PROJECT COST: \$2,000,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed May 2016
- DES** 70% Completed: Expected Completion date February 2017
- ROW** 50% Completed: Expected Completion date February 2017
- CON** 0% Completed: Expected Completion date December 2018

KERSHOPP1425 - 06-0Q620_ - Project Manager: Paul Pineda

I-5 - PM 62.5 / 73.1 -From Lerdo Overcrossing to Route 5/46 Separation - Replace PCC Panels, Grind Concrete Pavement & Crack Seal AC Shoulders

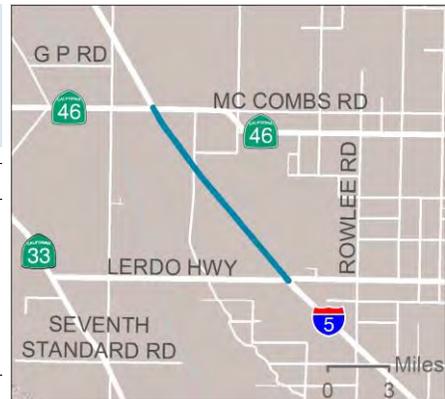


PROJECT COST: \$40,732,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed October 2011
- DES** 100% Completed: Completed September 2014
- ROW** 100% Completed: Completed September 2014
- CON** 70% Completed: Completion Expected by Summer 2017

KERSHOPP1414 - 06-0P140_ - Project Manager: Paul Pineda

I-5 - PM 36.1 / 41.2 - Kern County - Buena Vista Canal Road to SR 5/43 Separation Bridge - install median barrier

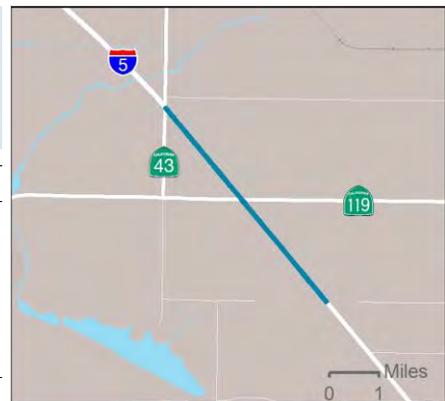


PROJECT COST: \$1,721,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed February 2015
- DES** 90% Completed: Expected Completion date is early 2016
- ROW** 100% Completed: Expected Completed January 2016
- CON** 80% Completed: Expected Completion date November 2016

KERSHOPP1427 - 06-0S650_ - Project Manager: Judy Aguilar

SR 14 - PM 16.6 - Mojave - Mojave Maintenance Station (L5713) construct crew facility

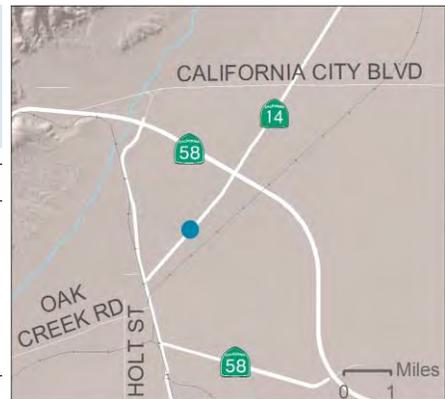

PROJECT COST: \$1,417,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed
- DES** 80% Completed: Expected Completion Fall 2017
- ROW** 80% Completed: Expected Completion Fall 2017
- CON** 0% Completed: Expected Completion Fall 2019

KERSHOPP1435 - 06-0T301 - Project Manager: Minerva Rodriguez

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Countywide - Highway Safety and Maintenance

SR 43 - PM 16.1 / 25.1 - In The Cities of Shafter and Wasco – ADA Curb Ramps



PROJECT COST: \$1,780,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed
- DES** 100% Completed: Completed May 2016
- ROW** 100% Completed: Completed August 2016
- CON** 0% Completed: Expected Completion Summer 2017

KERSHOPP1415 - 06-0P270_ - Project Manager: Chris Gardner

SR 43 - PM 0.1 / 0.4 - Bakersfield - SR 43/119 Intersection Improvements



PROJECT COST: \$7,200,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed October 2015
- DES** 0% Completed: Expected Completion January 2018
- ROW** 0% Completed: Expected Completion January 2018
- CON** 0% Completed: Expected Completion June 2019

KERSHOPP1426 - 06-0P900_ - Project Manager: Suzie Holdridge

SR 46 - PM 57.5 / 57.8 – Near Wasco - At SR 46/99 Separation - Bridge Replacement



PROJECT COST: \$17,000,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed September 2014
- DES** 95% Completed: Expected Completion by Fall 2016
- ROW** 70% Completed: Expected Completion by Fall 2016
- CON** 0% Completed: Expected Completion by Fall 2019

KERSHOPP1405 - 06-0K460_ - Project Manager: Chris Gardner

SR 58 - PM R55.4 / R59.7 - Kern County Near Bakersfield - Cottonwood Road to Undercrossing 0.3 miles east of SR 58/184 Separation - Pavement Rehabilitation



PROJECT COST: \$47,300,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed
- DES** 50% Completed: Expected Completion Date December 2016
- ROW** 30% Completed: Expected Completion Date January 2017
- CON** 0% Completed: Expected Completion Date August 2018

KERSHOPP1601 - 06-0S470_ - Project Manager: Suzie Holdridge

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Countywide - Highway Safety and Maintenance

SR 58 - PM R99.0 / R100 - Tehachapi - About 8 miles east of Tehachapi from Sand Canyon Overhead to 0.5 miles east of Cache Creek (BR# 50-346 L/R) - replace bridges




PROJECT COST: \$21,000,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed July 2015
- DES** 40% Completed: Expected Completion September 2018
- ROW** 30% Completed: Expected Completion January 2018
- CON** 0% Completed: Expected Completion March 2020

KERSHOPP1423 - 06-0Q190_ - Project Manager: Minerva Rodriguez

SR 58 - PM T52.1 / R52.3 - In Bakersfield - SR 58/99 Separation to Real Road - Install temporary K-Rail and Friction Treatment

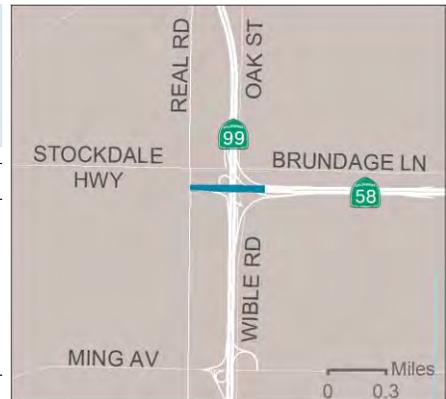

PROJECT COST: \$544,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed July 2014
- DES** 100% Completed: Completed January 2016
- ROW** 100% Completed: Completed January 2015
- CON** 5% Completed: Expected Completion November 2016

KERSHOPP1424 - 06-0R020_ - Project Manager: Paul Pineda

SR 58 - PM R52.7 / R55.5 - Bakersfield - SR 58/99 Separation to Cottonwood Road - Roadway Rehabilitation




PROJECT COST: \$21,325,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed
- DES** 100% Completed: Completed April 2016
- ROW** 100% Completed: Completed April 2016
- CON** 0% Completed: Expected Start Date Summer 2018

KERSHOPP1434 - 06-0G851_ - Project Manager: Minerva Rodriguez

SR 58 - PM R94.1 - Tehachapi - Near Tehachapi at Summit Overhead - Replace Bridge Rails

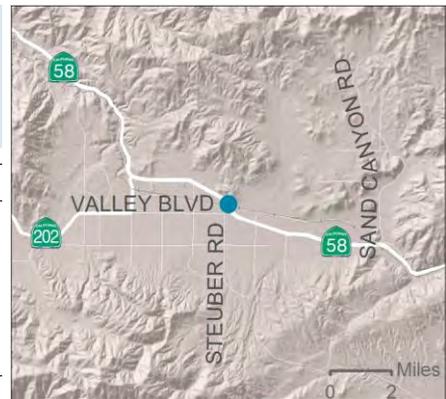

PROJECT COST: \$1,425,000 Cost estimates are subject to revision.


- ENV** 100% Completed: Completed
- DES** 40% Completed: Expected Completion Date Fall 2018
- ROW** 30% Completed: Expected Completion Date March 2018
- CON** 0% Completed: Expected Completion Date July 2019

KERSHOPP1422 - 06-0Q180_ - Project Manager: Minerva Rodriguez

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Countywide - Highway Safety and Maintenance

SR 58 - PM R88.5 / R99.8 - Near Tehachapi - Pavement Preservation (CAPM)

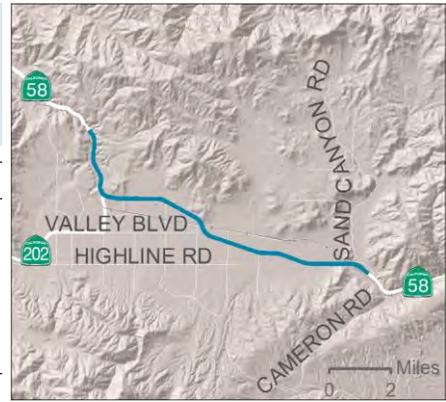

PROJECT COST: \$18,500,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed
- DES** 100% Completed: Expected Completion Date Fall 2015
- ROW** 100% Completed: Completed January 2015
- CON** 50% Completed: Expected Completion Date Summer 2017

KERSHOPP1429 - 06-0R150_ - Project Manager: Minerva Rodriguez

SR 99 - PM 49.6 – McFarland - At Kern Avenue Pedestrian Overcrossing on SR 99- ADA Compliance Upgrades




PROJECT COST: \$4,000,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed
- DES** 100% Completed: Completed August 2016
- ROW** 100% Completed: Completed May 2016
- CON** 0% Completed: Completion Expected by Summer 2017

KERSHOPP1403B - 06-0H642 - Project Manager: Paul Pineda

SR 99 - PM 24.1 / 28.4 - Bakersfield - Palm Avenue Overcrossing to Beardsley Canal - Roadway Rehabilitation

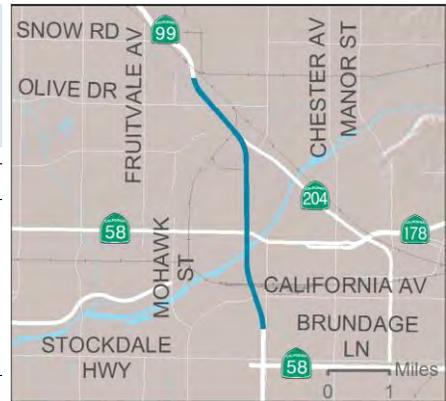


PROJECT COST: \$45,200,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed August 2016
- DES** 30% Completed: Expected Completion Date December 2017
- ROW** 10% Completed: Expected Completion Date March 2017
- CON** 0% Completed: Expected Completion Date March 2019

KERSHOPP1432 - 06-0Q280_ - Project Manager: Paul Pineda

SR 99 - PM 23.1 / 27.3 - Near Bakersfield, from Belle Terrace to Minkler Underpass Bridge No. 50-049.install highway lighting

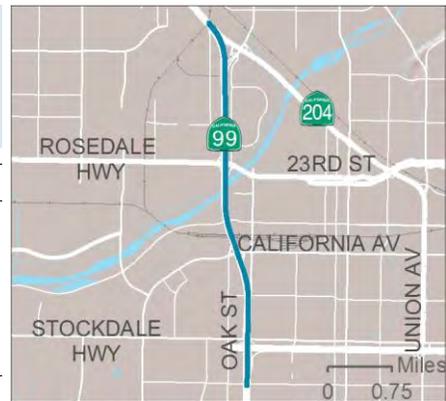

PROJECT COST: \$3,976,000 Cost estimates are subject to revision.


- ENV** 100% Completed: Completed
- DES** 5% Completed: Expected completion date is mid-2017
- ROW** 15% Completed: Expected completion by Mid-2017
- CON** 0% Completed: Expected Start date is Mid-2017

KERSHOPP120202A - 06-0S450 - Project Manager: Paul Pineda

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Countywide - Highway Safety and Maintenance

SR 99 - PM 26.7 – Bakersfield - Airport Drive Overcrossing and Golden State Avenue Separation - Seismic Restoration

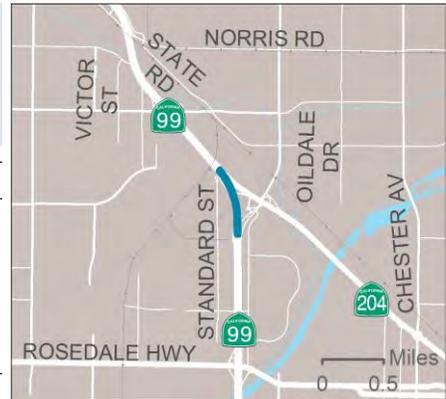


PROJECT COST: \$2,911,000 Cost estimates are subject to revision.

- ENV 100%** Completed: Completed
- DES 100%** Completed: Completed May 2016
- ROW 100%** Completed: Completed May 2016
- CON 0%** Completed: Completion Expected by Fall 2018

KERSHOPP1406 - 06-0K810_ - Project Manager: Judy Aguilar

SR 14, 58 and US 395: At Various Locations - install changeable message signs at four locations, southbound on US 395, eastbound on SR 58 and northbound on SR 14.

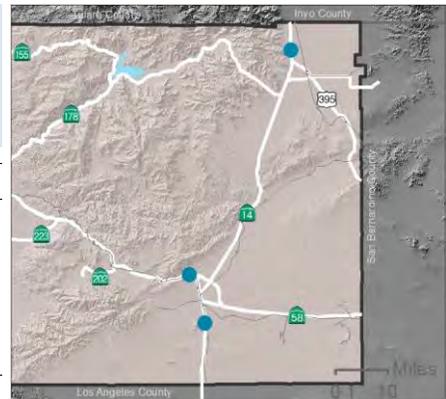


PROJECT COST: \$2,078,000 Cost estimates are subject to revision.

- ENV 100%** Completed: Completed December 2014
- DES 100%** Completed: Completed March 2012
- ROW 100%** Completed: Completed December 2014
- CON 40%** Completed: Completion expected by December 2016

KERSHOPP1437 - 09-36450 - Project Manager: Brian McElwain

SR 155 - PM 1.5 - Near Delano at Browning Road - Intersection Improvements

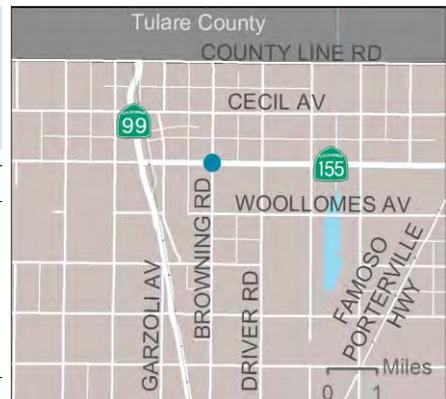


PROJECT COST: \$2,800,000 Cost estimates are subject to revision.

- ENV 100%** Completed: Completed in Summer 2014
- DES 95%** Completed: Expected Completion by Spring 2017
- ROW 95%** Completed: Expected Completion by Spring 2017
- CON 0%** Completed: Expected Completion by Fall 2018

KERSHOPP1416 - 06-0P290_ - Project Manager: Chris Gardner

SR 204 - PM 5.4 / 6.7 -From SR-99 to SR-178 at Various Locations - Place Deck Overlay, Replace Joint Seals & Paint

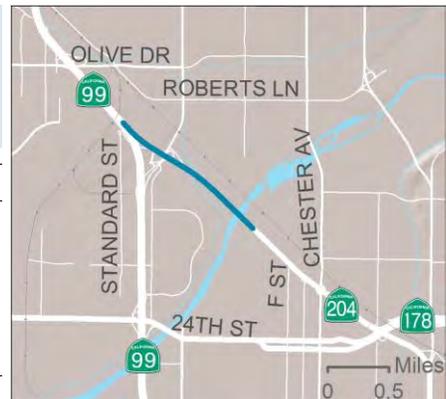

PROJECT COST: \$9,347,000 Cost estimates are subject to revision.

- ENV 100%** Completed: Completion Expected by Spring 2014
- DES 100%** Completed: Completion Expected by Spring 2015
- ROW 100%** Completed: Completion Expected by Spring 2015
- CON 40%** Completed: Completion Expected by June 2017

KERSHOPP1413 - 06-0N960_ - Project Manager: Paul Pineda

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Countywide - Highway Safety and Maintenance

SR 223 - PM 21.0 / 21.3 - In and Near Arvin, at Derby Street - Install traffic signals



PROJECT COST: \$2,603,000 Cost estimates are subject to revision.

ENV 100% Completed: Expected completion date August 2015


DES 30% Completed: Expected completion date January 2018

ROW 10% Completed: Expected completion date February 2018

CON 0% Completed: Expected start date February 2018

KERSHOPP120202B - 06-0S510 - Project Manager: Paul Pineda


Summary Project Map: Countywide - Highway Safety and Maintenance

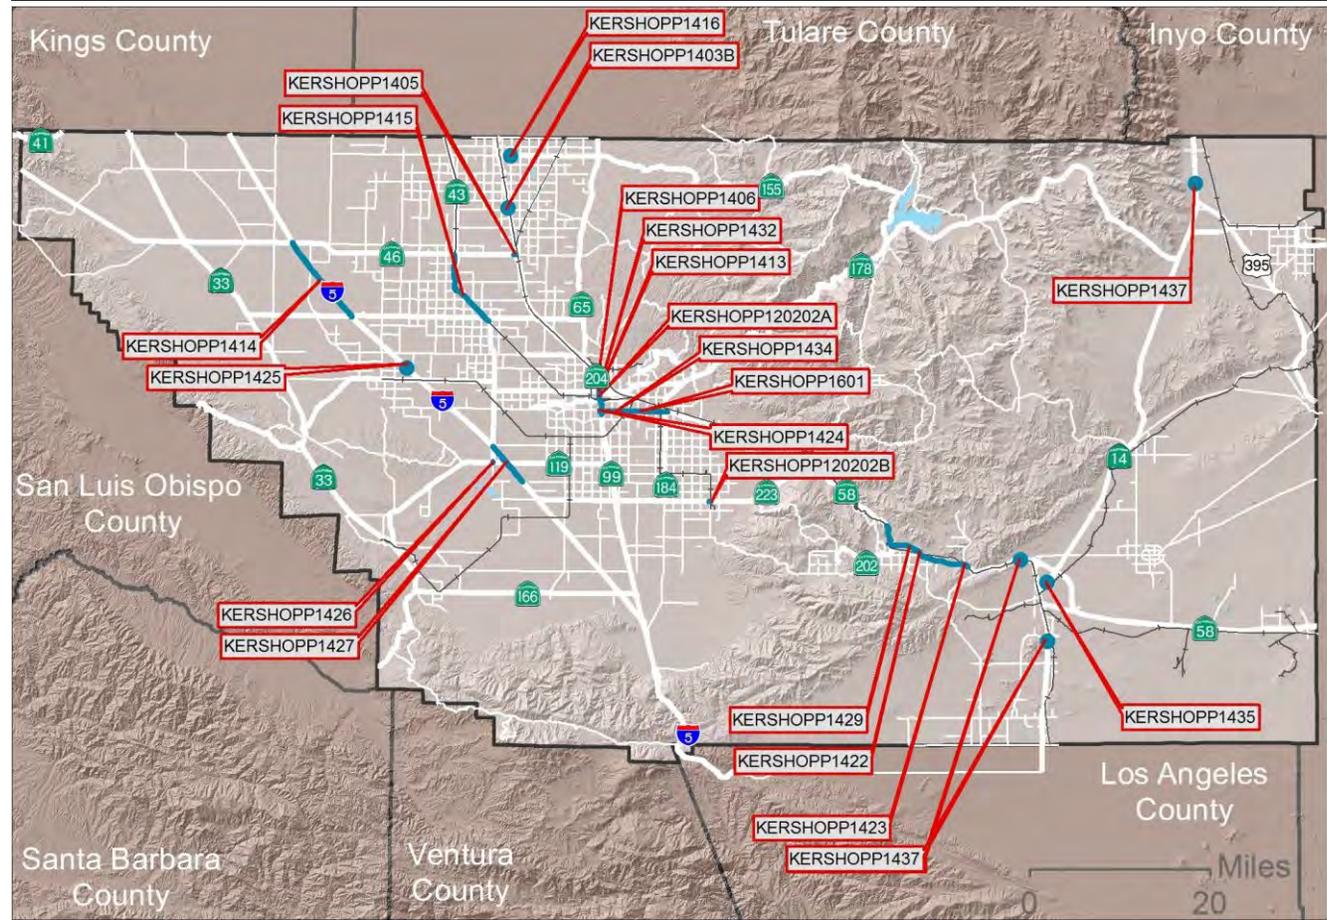

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Highway Projects Completed in Last Two Years

Westside Parkway - Construct a new freeway from Heath Road to Allen Road (Phase 6).

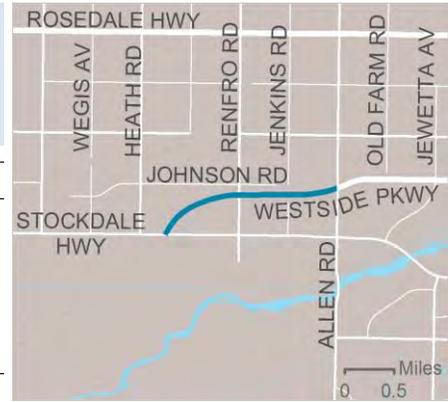

PROJECT COST: \$38,000,000 Cost estimates are subject to revision.

- ENV 100%** Completed:
- DES 100%** Completed:
- ROW 100%** Completed:
- CON 100%** Completed: Completed April 2015

KER080107 - - Project Manager: Luis Topete

I-5: Near Fort Tejon to 1.1 miles south of Grapevine undercrossing - Grapevine Escape Ramp Extinguishable Message Signs upgrade




PROJECT COST: \$1,500,000 Cost estimates are subject to revision.

- ENV 100%** Completed: Completed in 2013
- DES 100%** Completed: Completed February 2014
- ROW 100%** Completed: Completed February 2014
- CON 100%** Completed: Completed construction April 2015

KER130202 - 06-0Q450 - Project Manager: Paul Pineda

I-5 - R15.8 / 82.3 - On Routes 5, 99, 58 and 204 at Various Locations - Wire Theft Restoration

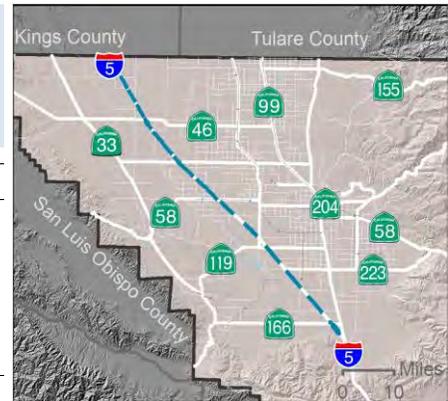


PROJECT COST: \$1,660,000 Cost estimates are subject to revision.

- ENV 100%** Completed: Completed November 2013
- DES 100%** Completed: Completed September 2014
- ROW 100%** Completed: Completed September 2014
- CON 100%** Completed: Expected Completed August 2015

KERSHOPP1421 - 06-0Q580_ - Project Manager: Anand Kapoor

SR 14 - PM 39.9 - Red Rock Canyon - bridge replacement due to scouring

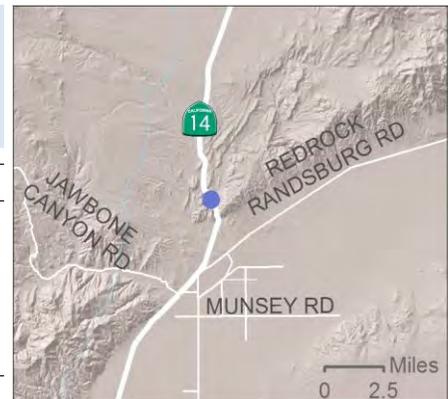

PROJECT COST: Cost estimates are subject to revision.

- ENV 100%** Completed:
- DES 100%** Completed:
- ROW 100%** Completed:
- CON 100%** Completed: Completed in January 2015

KERSHOPP1317 - 06-0H180 - Project Manager: Minerva Rodriguez

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Highway Projects Completed in Last Two Years

SR 58 - PM 36.3 / 39.9 - From Gatson Street to SR 43 - Widen Shoulders & Install Rumble Strips




PROJECT COST: \$4,300,000 Cost estimates are subject to revision.

- ENV 100%** Completed: Completed in November 2012
- DES 100%** Completed: Expected Completed Spring 2014
- ROW 100%** Completed: Expected Completed Spring 2014
- CON 100%** Completed: Expected Completed September 2015

KERSHOPP1418 - 06-0P560_ - Project Manager: Chris Gardner

SR 58, 99, 178 - PM 0 - Upgrade Sign Panels at Various Locations on SR 58, 99 and 178

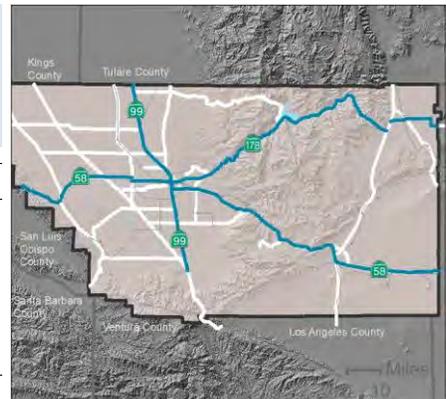

PROJECT COST: \$3,265,000 Cost estimates are subject to revision.

- ENV 100%** Completed:
- DES 100%** Completed: Completed Spring 2015
- ROW 100%** Completed: Completed Spring 2015
- CON 100%** Completed: Completed June 2016

KERSHOPP1433 - 06-0S750_ - Project Manager: Emad Abi-Rached

SR 58 - PM 136.0 / 143.8 - Near Boron - From 0.4 miles west of West Boron overcrossing to San Bernardino County Line - Rubberized Asphalt Concrete Overlay




PROJECT COST: \$5,200,000 Cost estimates are subject to revision.

- ENV 100%** Completed: Completed December 2014
- DES 100%** Completed: Expected Completion Date Spring 2015
- ROW 100%** Completed: Completed March 2015
- CON 100%** Completed: Completed June 2016

KERSHOPP1430 - 06-0S280_ - Project Manager: Emad Abi-Rached

SR 58 - PM R85.1 - Tehachapi - Broome Road - Widen intersection to accommodate permit loads

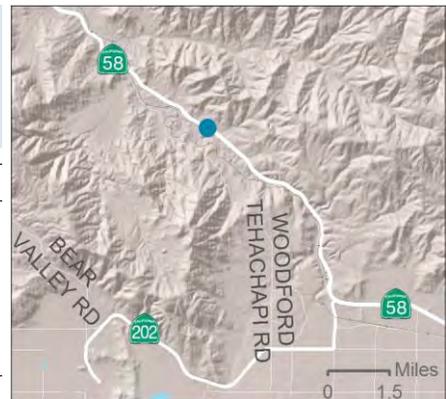

PROJECT COST: \$1,457,000 Cost estimates are subject to revision.


- ENV 100%** Completed: Completed
- DES 100%** Completed: Completed October 2014
- ROW 100%** Completed: Completed
- CON 100%** Completed: Completed May 2015

KERSHOPP1436 - 06-0P070_ - Project Manager: Minerva Rodriguez

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Highway Projects Completed in Last Two Years

SR 58 - PM 94.4 - Tehachapi Summit Interchange - Widen Intersection

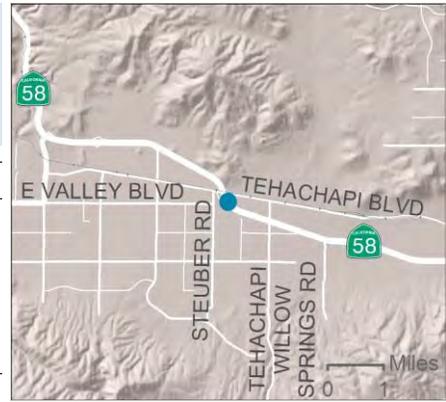

PROJECT COST: \$3,328,000 Cost estimates are subject to revision.

- ENV 100%** Completed: Completed May 2013
- DES 100%** Completed: Completed December 2014
- ROW 100%** Completed: Completed December 2014
- CON 100%** Completed: Completed October 2015

KERSHOPP1412 - 06-0N560_ - Project Manager: Minerva Rodriguez

SR 58 - R99.3 / R99.7 - East Bound Sand Canyon Bridge / Bridge Replacement




PROJECT COST: \$8,422,000 Cost estimates are subject to revision.

- ENV 100%** Completed: Completed in October 2011
- DES 100%** Completed: Completed Summer 2015
- ROW 100%** Completed: Completed October 2014
- CON 100%** Completed: Completed June 2016

KERSHOPP1409 - 06-0M2604 - Project Manager: Minerva Rodriguez

SR 58 - PM R52.4 / R55.5 - Centennial Corridor - Gap Closure Widening from SR 99 to Cottonwood Rd - widen freeway from 4 to 5 lanes

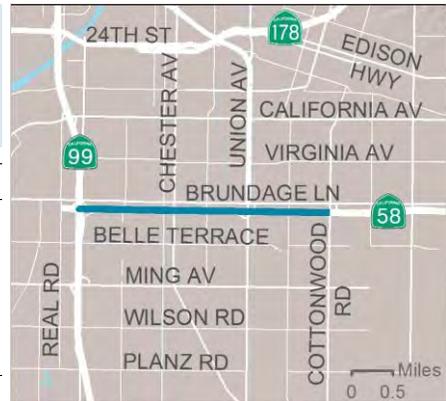


PROJECT COST: \$23,330,000 Cost estimates are subject to revision.

- ENV 100%** Completed:
- DES 100%** Completed:
- ROW 100%** Completed:
- CON 100%** Completed: Completed April 2015

KER120101 - EA 06-0G850 - Project Manager: Paul Pineda / Luis Topete

SR 99 - PM R46.9 / 48.6 - Near Famoso south of McFarland from Sherwood Avenue Overcrossing to Whisler Road Overcrossing - Construct Rumble Strip

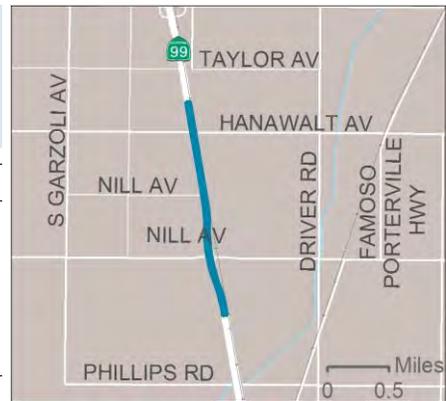

PROJECT COST: \$1,800,000 Cost estimates are subject to revision.


- ENV 100%** Completed:
- DES 100%** Completed: November 2013
- ROW 100%** Completed: November 2013
- CON 100%** Completed: December 2014

KERSHOPP1417 - 06-0P300_ - Project Manager: Chris Gardner

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Highway Projects Completed in Last Two Years

SR 99 - PM 21.6 / 24.7 – Bakersfield - Various locations from Planz Road Overcrossing to California Ave Undercrossing - Freeway Maintenance Access

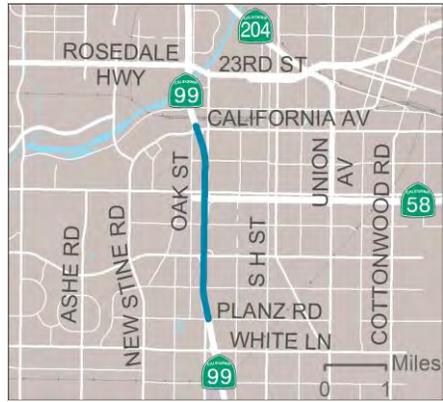

PROJECT COST: \$1,600,000 Cost estimates are subject to revision.

- ENV 100%** Completed:
- DES 100%** Completed: Completed by July 2015
- ROW 100%** Completed: Completed February 2015
- CON 100%** Completed: Completed March 2016

KERSHOPP1402 - 06-0E340_ - Project Manager: Chris Gardner

SR 99 - PM 18.0 / 19.2 - Bakersfield on State Route 99 at Hosking Road - Construct a new interchange




PROJECT COST: \$31,000,000 Cost estimates are subject to revision.

- ENV 100%** Completed:
- DES 100%** Completed:
- ROW 100%** Completed:
- CON 100%** Completed: Completed March 2016

KER090601 - 06-0C930 - Project Manager: Luis Topete / Paul Pineda

SR 178 - PM 100.6 / 102.7 - From China Lake Blvd to Gemstone Street In Ridgecrest - Reconstruct Center Median With Raised Center Median

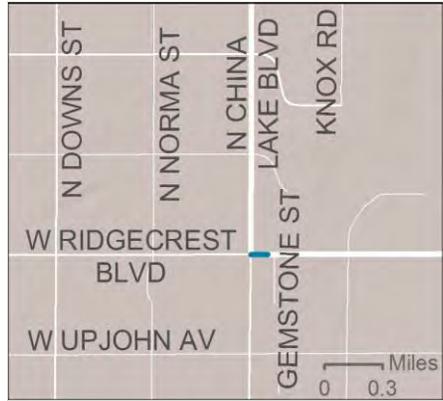


PROJECT COST: \$3,126,000 Cost estimates are subject to revision.

- ENV 100%** Completed: Completed in June 2013
- DES 100%** Completed: Completed Summer 2014
- ROW 100%** Completed:
- CON 100%** Completed: Completed August 2015

KERSHOPP1419 - 06-0P810_ - Project Manager: Minerva Rodriguez

SR 178 - PM R4.4 – Bakersfield - Sunny Lane Pedestrian Overcrossing on SR 178 - ADA Compliance Upgrades

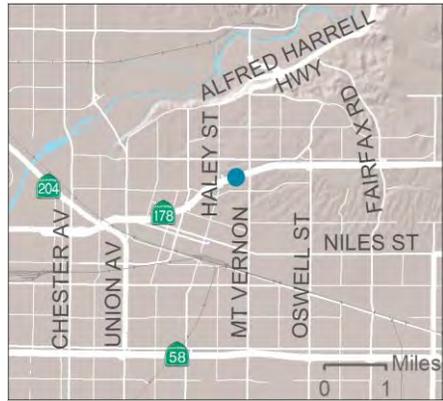

PROJECT COST: \$2,901,000 Cost estimates are subject to revision.


- ENV 100%** Completed:
- DES 100%** Completed:
- ROW 100%** Completed:
- CON 100%** Completed: Completed June 2016

KERSHOPP1403A - 06-0H641 - Project Manager: Paul Pineda

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Highway Projects Completed in Last Two Years

SR 178 - PM R7.0 / T9.1 - SR 178 at Morning Drive - Construct new Interchange and widen SR 178

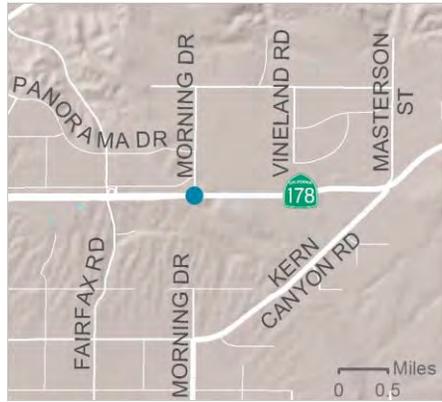


PROJECT COST: \$56,000,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed in 2012
- DES** 100% Completed: Completed in 2013
- ROW** 100% Completed: Completed in 2013
- CON** 100% Completed: Completed September 2015

KER050106 - EA 06-0C940 - Project Manager: Kris Budak / Minerva Rodriguez

SR 223 - PM 4.8 / R17.2 - From Old River Road to Vineland Road - Widen Shoulders & Install Rumble Strips

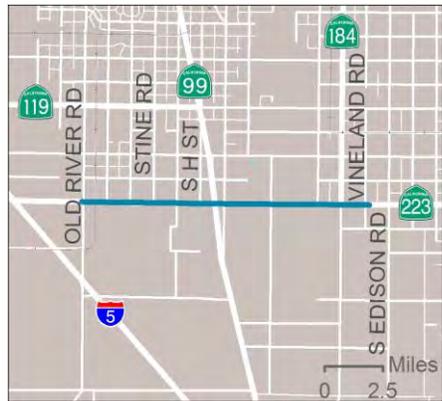

PROJECT COST: \$5,100,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed
- DES** 100% Completed: Completed
- ROW** 100% Completed: Completed
- CON** 100% Completed: Completed June 2015

KERSHOPP1420 - 06-0P840_ - Project Manager: Chris Gardner

US 395 - PM 0.0 / 23.4 - Johannesburg - San Bernardino County Line to SR 178 - Rubberized Asphalt Concrete Overlay




PROJECT COST: \$7,320,000 Cost estimates are subject to revision.

- ENV** 100% Completed: October 2014
- DES** 100% Completed: Completed February 2015
- ROW** 100% Completed: Completed February 2015
- CON** 100% Completed: Completed August 2016

KERSHOPP1431 - 06-0S270_ - Project Manager: Emad Abi-Rached

Highway Projects Completed in Last Two Years

Summary Project Map: Highway Projects Completed in Last Two Years

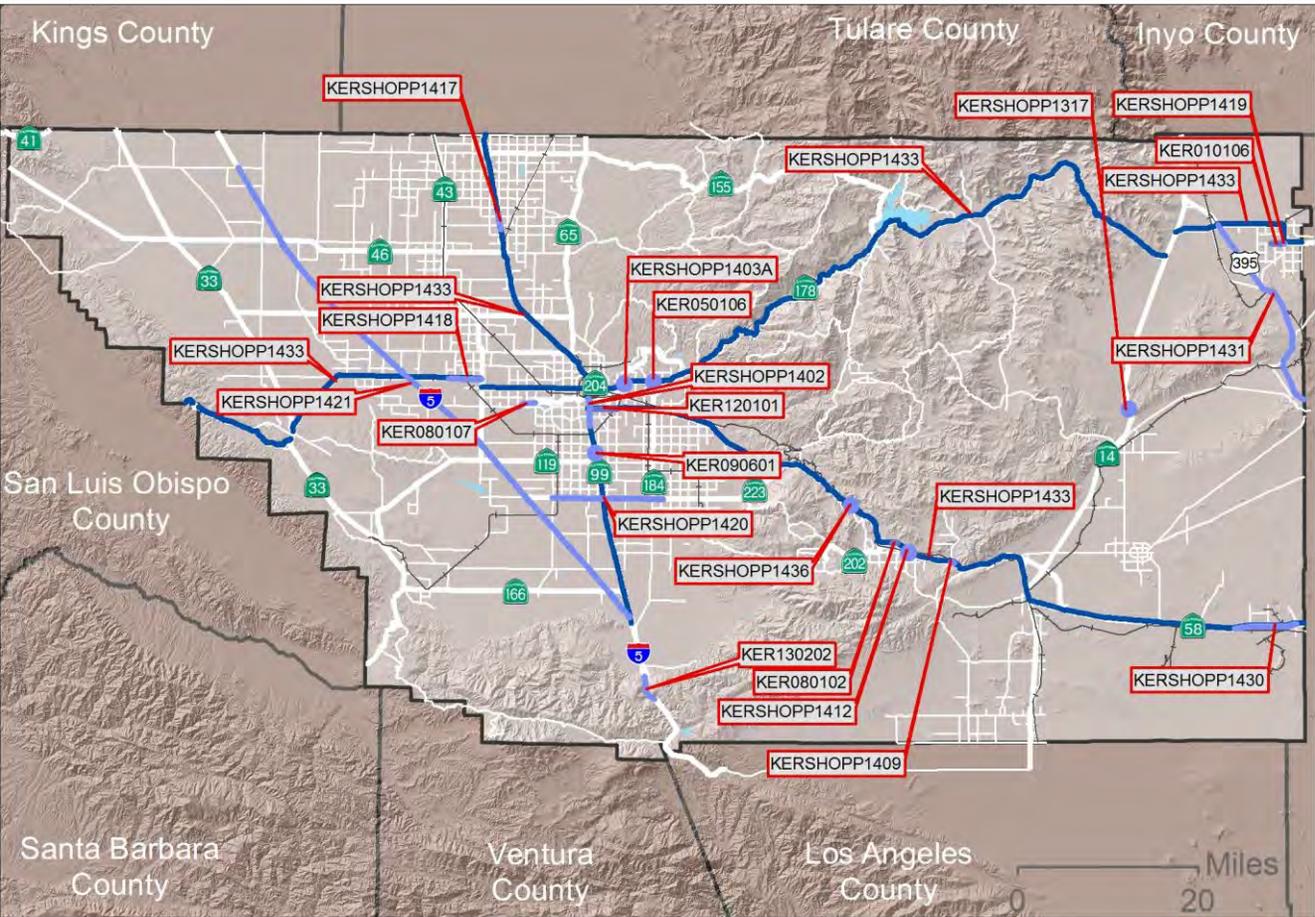

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Regional Area - Countywide Non-Metro

SR 14 - PM 58.3 / 62.3 - Freeman Gulch Widening Segment 1 - (4 miles) - 0.5 miles north of SR 178 west to 1.7 miles north of Route 178 east - widen to four lanes



PROJECT COST: \$45,000,000 Cost estimates are subject to revision.

- ENV** 100% Completed:
- DES** 100% Completed: Completed April 2016
- ROW** 100% Completed: Completed April 2016
- CON** 0% Completed: Estimated start date is January 2017

KER010103 - EA 06-45711 - Project Manager: Minerva Rodriguez

SR 46 - PM 30.5 / 33.5 - Route 46 Expressway (3 miles) - from east of Brown Material Road to east of Interstate 5 - widen to 4 lanes & improve ramp (segment 4A)



PROJECT COST: \$34,000,000 Cost estimates are subject to revision.

- ENV** 100% Completed:
- DES** 95% Completed: Expected completion date is March 2017
- ROW** 65% Completed: Expected completion date is March 2017
- CON** 0% Completed: Expected completion date is August 2020

KER060103 - EA 06-44254 - Project Manager: Neil Bretz

SR 46 – Wasco Four Lane Widening (5 miles) - In the City of Wasco, widen from two to four lanes from Jumper Ave to State Route 43



PROJECT COST: \$95,200,000 Cost estimates are subject to revision.

- ENV** 100% Completed:
- DES** 0% Completed: Not yet programmed
- ROW** 0% Completed: Not yet programmed
- CON** 0% Completed: Not yet programmed

KER990105 - EA 06-41880 - Project Manager: Neil Bretz

SR 58 at Dennison Road - construct new interchange to provide alternative access to the City of Tehachapi (substitute frontage road for short-term solution - see Challenger Drive)



PROJECT COST: \$25,544,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Shelved due to funding constraints
- DES** 0% Completed: Inactive due to lack of funding
- ROW** 0% Completed: Not yet programmed; start date not determined
- CON** 0% Completed: Not yet programmed; start date not determined

KER990106 - EA 06-425500 - Project Manager: Minerva Rodriguez

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Regional Area - Countywide Non-Metro

SR 119 - PM R10.0 / R13.3 - Cherry Ave 4-Lane - from Cherry Avenue to 0.40 miles east of Elk Hills Road (Phase 1) construct truck climbing / passing lanes at various locations



PROJECT COST: \$8,238,000 Cost estimates are subject to revision.

- ENV** 100% Completed:
- DES** 100% Completed: Completed 2015
- ROW** 100% Completed: Completed 2015
- CON** 70% Completed: Completion expected by winter 2016

KER990102 - EA 06-42471 - Project Manager: Paul Pineda

SR 119 Cherry Ave 4-Lane - from Cherry Avenue to 0.40 miles east of Elk Hills Road (Phase 2) construct 4-lane bypass (4 miles)



PROJECT COST: \$66,000,000 Cost estimates are subject to revision.

- ENV** 100% Completed:
- DES** 0% Completed: This phase was deferred.
- ROW** 0% Completed: Not yet funded; start date not determined
- CON** 0% Completed: Not yet funded; start date not determined

KER990102 - EA 06-424700 - Project Manager: Victor Shaw

U.S. 395 Inyokern 4-Lane (9 miles) - from Highway 14 to China Lake Blvd. - widen from two to four lanes




PROJECT COST: \$183,500,000 Cost estimates are subject to revision.

- ENV** 80% Completed: Shelved due to funding constraints
- DES** 0% Completed: Not yet funded; start date not determined
- ROW** 0% Completed: Not yet funded; start date not determined
- CON** 0% Completed: Not yet funded; start date not determined

KER010104 - EA 06-443100 - Project Manager: Minerva Rodriguez

Regional Area - Countywide Non-Metro

Summary Project Map: Regional Area - Countywide Non-Metro

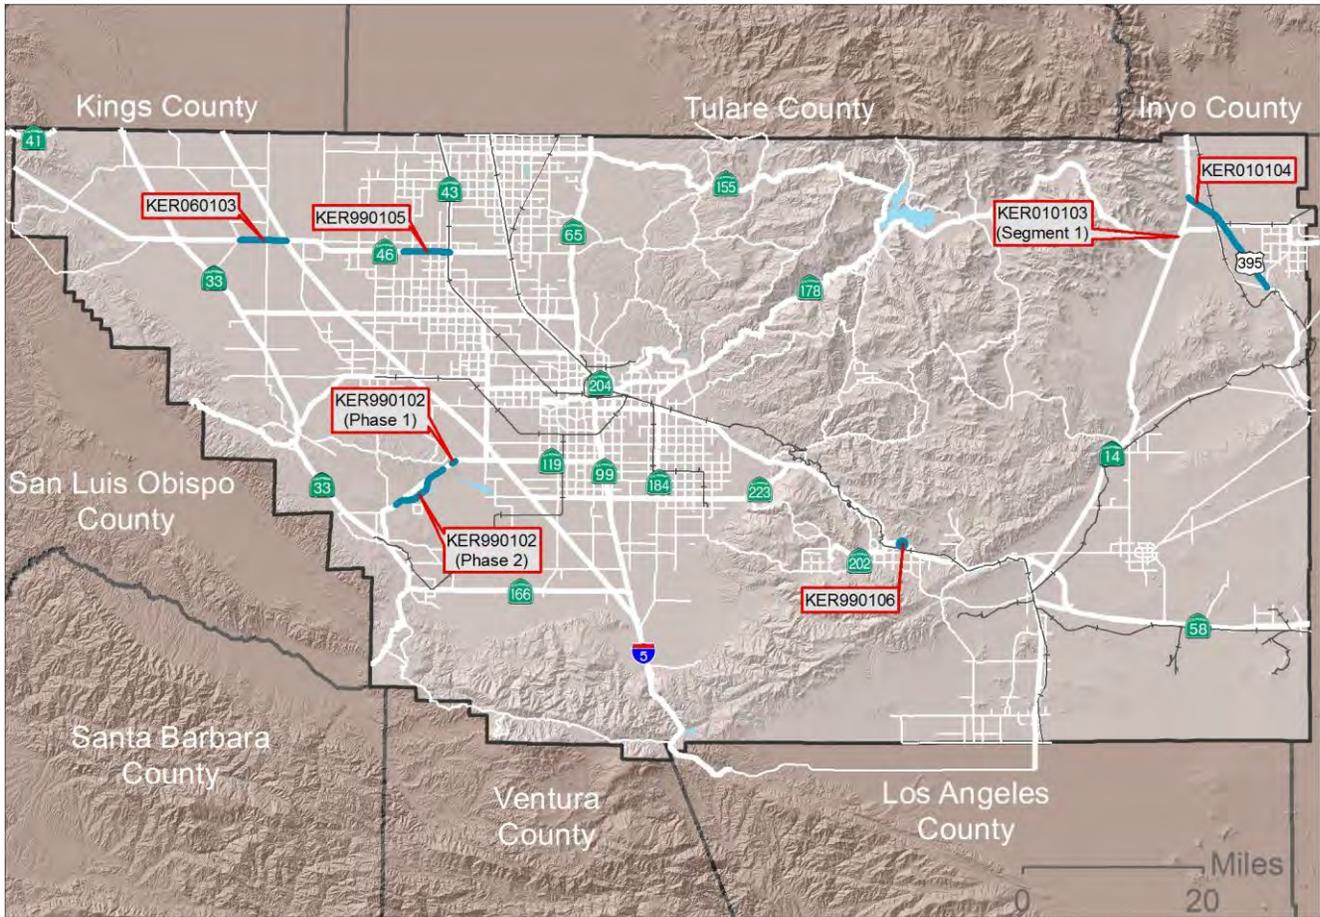

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Regional Area - Metropolitan Bakersfield - Thomas Road Improvement Program or "TRIP"

Hageman Flyover - extend Hageman Road east to SR 204 / Golden State Avenue.



PROJECT COST: \$73,000,000 Cost estimates are subject to revision.

- ENV** 100% Completed:
- DES** 65% Completed: Estimated completion date Mid 2017
- ROW** 20% Completed: Estimated completion date Mid 2017
- CON** 0% Completed: Expected start date in Late 2017

KER020604 - EA 06 - 4845 - Project Manager: Kris Budak / Minerva Rodriguez

SR 58 - PM T31.7 / R55.6 - Centennial Corridor - Connector from Westside Parkway to SR 58/99 - Construct a new 6-lane freeway on an 8-lane right-of-way



PROJECT COST: \$689,000,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed January 2016
- DES** 65% Completed: Expected completion date Mid 2017
- ROW** 60% Completed: Expected completion date Mid 2017
- CON** 0% Completed: Expected start date in late 2017

KER080109 - EA 06-48460 - Project Manager: Minerva Rodriguez / Luis Topete

SR 58 - PM R52.3 / R55.4 - In Bakersfield: Along SR 58 and SR 99 - Beltway Operational improvements (SR 58 GAP closure - an element of the Bakersfield Beltway system)



PROJECT COST: \$125,860,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed February 2014
- DES** 100% Completed: Completion Summer 2014
- ROW** 100% Completed: Completion Summer 2014
- CON** 30% Completed: Expected completion date in Fall 2017

KER130106 - 06-48461 - Project Manager: Paul Pineda / Luis Topete

SR 58 - PM 46.1 / 51.7 - Rosedale Highway - from Calloway to State Route 99 - widen to 6 lanes



PROJECT COST: \$29,700,000 Cost estimates are subject to revision.

- ENV** 100% Completed:
- DES** 100% Completed:
- ROW** 100% Completed: December 2014
- CON** 98% Completed: Expected completion date in Fall 2016

KER080110 - EA 06-0F3600 - Project Manager: Kris Budak / Paul Pineda

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Regional Area - Metropolitan Bakersfield - Thomas Road Improvement Program or "TRIP"

SR 178 - PM 0.4 / 1.9 - 24th & 23rd St (SR 178/99) to M St Widening and Intersection Improvements TRIP



PROJECT COST: \$43,500,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed in March 2014
- DES** 65% Completed: Expected completion date is Late 2015
- ROW** 86% Completed: Expected completion date is Summer 2016
- CON** 0% Completed: Expected start date in Fall 2016

KER050110 - EA 06-48470 - Project Manager: Kris Budak / Paul Pineda

SR 178 - PM R8.4 / T9.8 - SR 178 - widen from two lanes to six lanes between Canteria Dr./ Bedford Green Dr. and Masterson St and two to four lanes between Masterson St and Miramonte Dr.




PROJECT COST: \$36,500,000 Cost estimates are subject to revision.

- ENV** 100% Completed: Completed August 2012
- DES** 100% Completed: Expected completion date in Late 2014
- ROW** 100% Completed: Completed March 2015
- CON** 60% Completed: Expected completion date in summer 2017

KER050108 - EA 06-0F350 - Project Manager: Kris Budak / Minerva Rodriguez

Regional Area - Metropolitan Bakersfield - Thomas Road Improvement Program or "TRIP"

Summary Project Map: Regional Area - Metropolitan Bakersfield - Thomas Road Improvement Program or "TRIP"

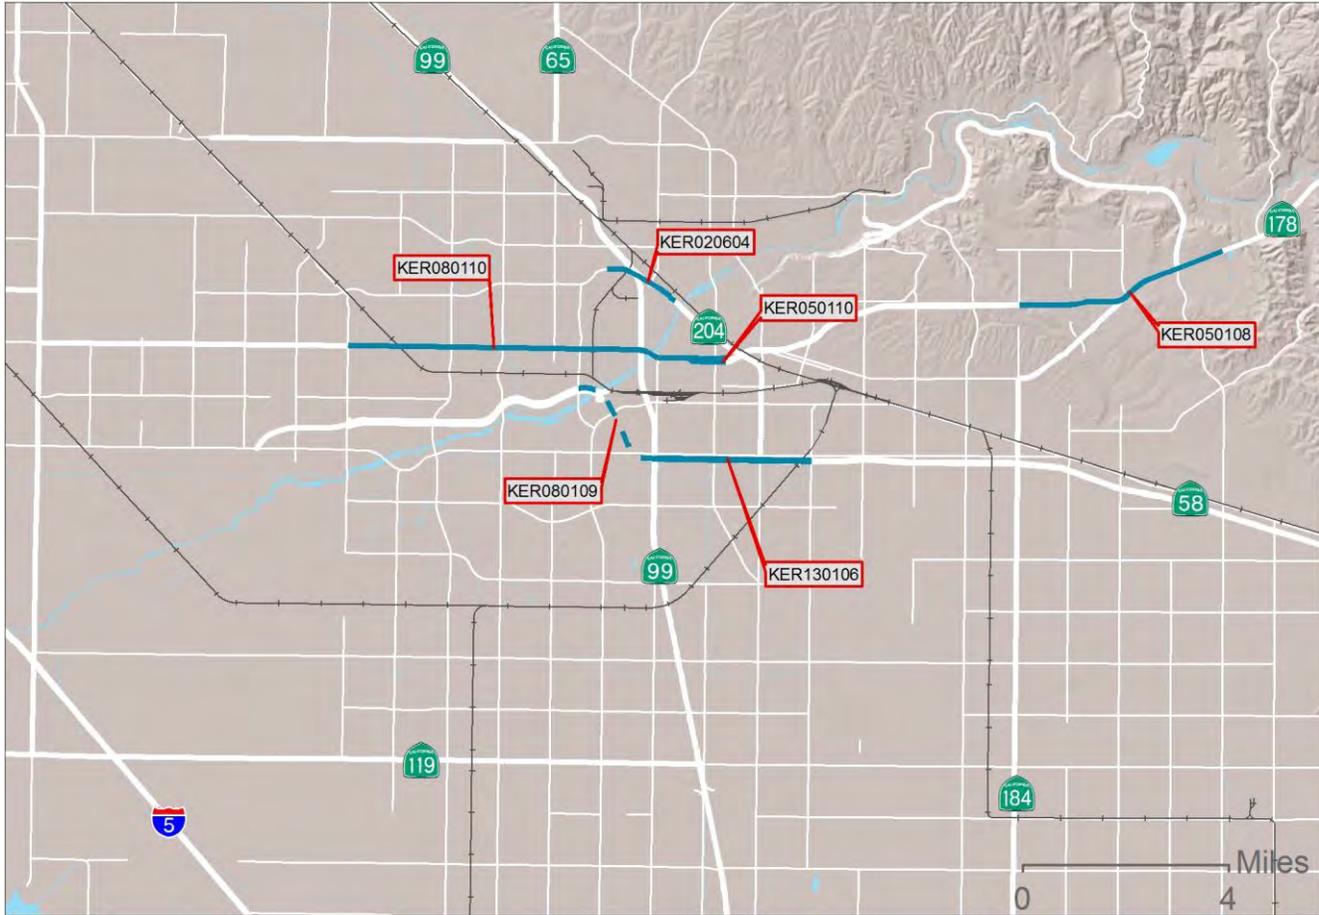

PROGRESS REPORT FOR PROJECTS OF REGIONAL SIGNIFICANCE - OCTOBER 2016

Regional Area - Metropolitan Bakersfield Area

SR 184 Weedpatch Widening (4 miles)- from Panama Lane to State Route 223 - widen from two to four lanes



PROJECT COST: \$32,000,000 Cost estimates are subject to revision.

ENV 100% Completed: This project has been shelved


DES Completed: Not yet funded; start date not determined

ROW Completed: Not yet funded; start date not determined

CON Completed: Not yet funded; start date not determined

KER990104 - EA 06-42480 - Project Manager: Minerva Rodriguez

Summary Project Map: Regional Area - Metropolitan Bakersfield Area

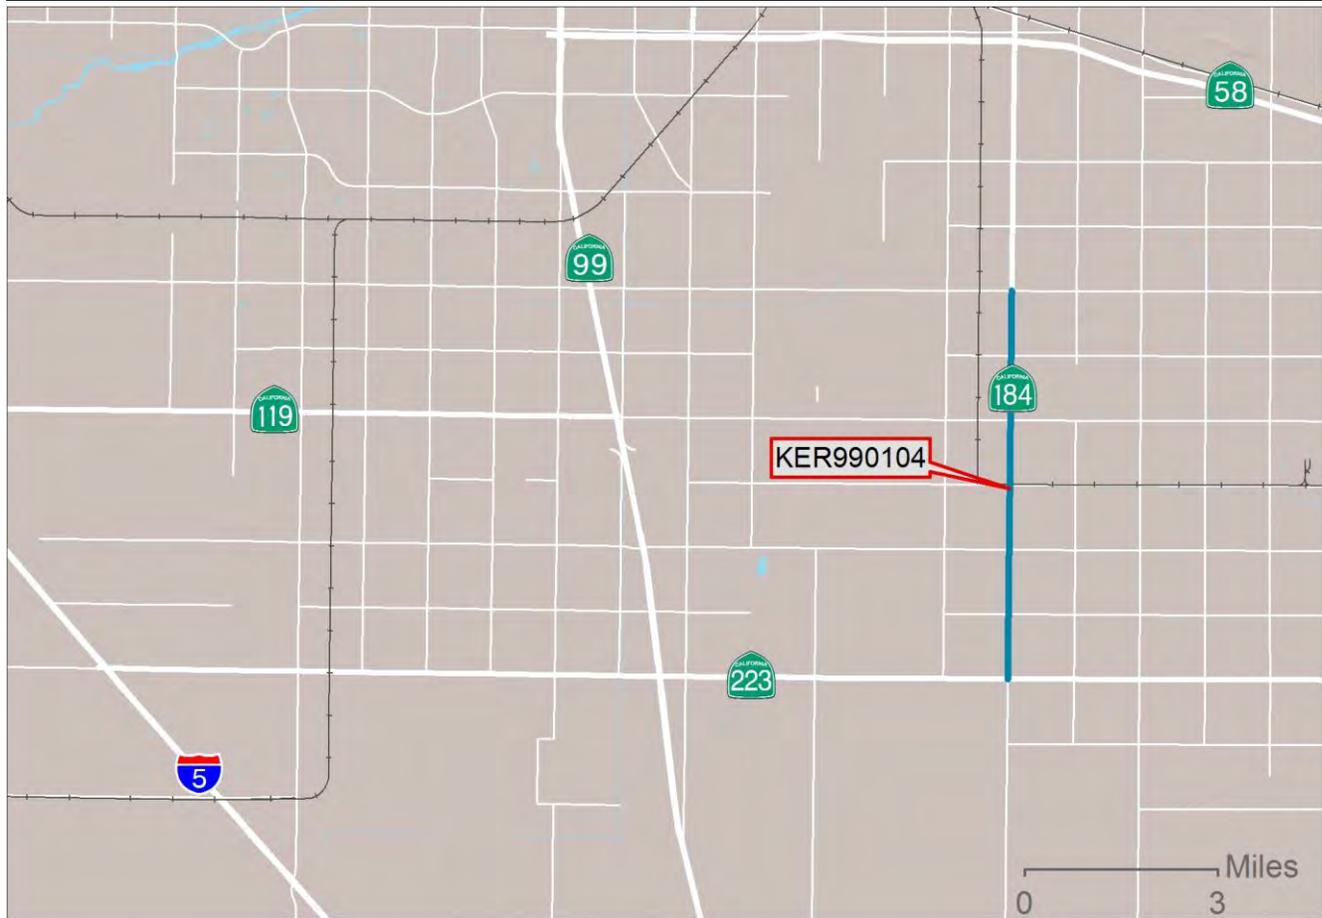



Morning Drive Interchange State Route 178 - February 2016

Kern Council of Governments Progress Report for Projects of Regional Significance

OCTOBER 2016 EDITION

RECENT PROJECT PHOTOS



SR 178 Widening
westbound east of
SR-184
NE Bakersfield
MAY 2016



SR 99 Beltway
Operational
Improvements
June 2016



SR 178 Pedestrian
Crossing at
Sunny Lane
June 2016

This progress report is updated and distributed to the Kern Council of Governments Board of Directors and the general public, on a quarterly basis. The listed projects are funded through a combination of local, state and federal transportation programs.

These projects add new lanes to existing highways, construct new roadways and maintain or improve existing roadways or related infrastructure. Cost estimates provided in the following pages include costs for construction, rights-of-way, design and support costs.

This report may be downloaded by visiting Kern COG's website at: www.kerncog.org. The report link is located towards the bottom of the home page under the "Projects of Regional Significance" section.

